



CEDAR RAPIDS, IOWA FLOOD RISK MANAGEMENT PROJECT



Cedar Rapids - Flood Risk Management Project

Feature Quantities	Total	Active			% Design Complete	% Construction Complete
		Construction	Complete	Remaining		
Levee (ft)	8,962	2,231	3,721	3,010	99%	42%
Floodwall (ft)	10,678	-	2,434	8,244	91%	23%
Pump Station (#)	7	1	2	4	98%	29%
Road Closures (#)	8	1	2	5	98%	25%
Railroad Closures (#)	4	1	-	3	88%	0%
Channel Modification (ft)	2,974	-	-	2,974	100%	0%

Current Status

Pump Station Status


- Completed Work
- Remaining Work

Alignment

- Alignment

Feature Status

- Completed Work
- Remaining Work

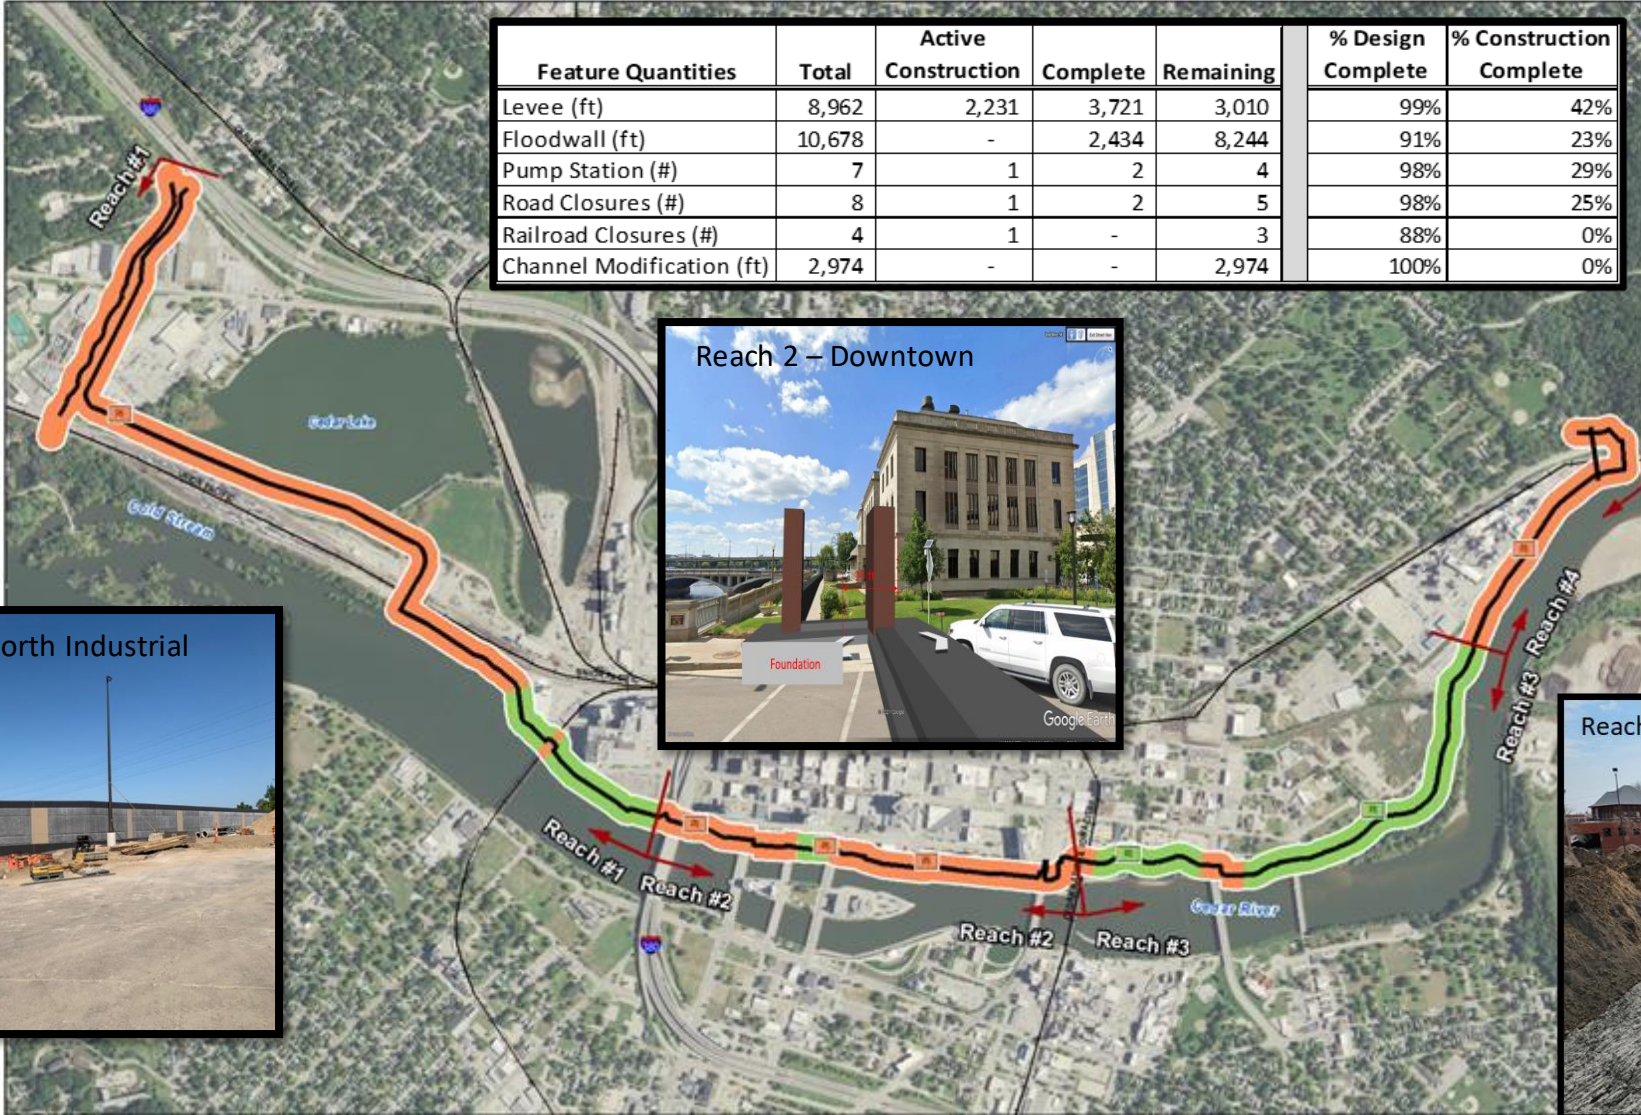

(As of APR 2022)
